


ID	Task Mode	Task Number	Deliverable Number	Task Name	Duration	Start	Finish	2019 Qtr 2   2019 Qtr 3   2019 Qtr 4   2020 Qtr 1   2020 Qtr 2   2020 Qtr 3   2020 Qtr 4   2021 Qtr 1   2021 Qtr 2																										
								Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun
1		1		<b>Project Management</b>	562.25 days	Wed 19-05-01	Fri 21-06-25																											
2			1	<a href="#">Kick-Off Meeting Agenda, Materials and Notes</a>	20 days	Wed 19-05-01	Wed 19-05-29																											
3		1.1		Kick-off Meeting	0 days	Wed 19-05-29	Wed 19-05-29																											
4		1.2		Work Plan	40 days	Mon 19-07-01	Fri 19-08-23																											
5			2	<a href="#">Project Work Plan (Draft and Final)</a>	0 days	Fri 19-08-23	Fri 19-08-23																											
6		1.3		Schedule	40 days	Mon 19-07-01	Fri 19-08-23																											
7			3	<a href="#">Project Schedule (Draft and Final)</a>	0 days	Fri 19-08-23	Fri 19-08-23																											
8		1.4		Project Management Meetings	435 days	Thu 19-09-12	Thu 21-05-13																											
30		1.5		Project Budget Tracking & Invoicing	520 days	Mon 19-07-01	Fri 21-06-25																											
31		1.6		Progress Reporting	520 days	Mon 19-07-01	Fri 21-06-25																											
32		1.7		File Sharing, Document Control, Quality Assurance	500 days	Mon 19-07-01	Fri 21-05-28																											
33			4	<a href="#">QA/QC Plan (Draft and Final)</a>	0 days	Fri 19-08-23	Fri 19-08-23																											
34		2		<b>Stakeholder Coordination and Public Outreach</b>	500 days	Mon 19-07-01	Fri 21-05-28																											
35		2.1		Stakeholder Engagement Plan (SEP)	40 days	Mon 19-07-01	Fri 19-08-23																											
36			1	<a href="#">Stakeholder Engagement Plan (SEP) (Draft and Final)</a>	0 days	Mon 19-08-26	Mon 19-08-26																											
37		2.2		Network Advisory Committee	390 days	Mon 19-11-04	Mon 21-05-03																											
45		2.3		Briefings and Outreach Meetings	500 days	Mon 19-07-01	Fri 21-05-28																											
46		3		<b>Existing Conditions</b>	210 days	Mon 19-07-01	Fri 20-04-17																											
47		3.1		Existing Conditions Analysis (1/2)	90 days	Mon 19-07-01	Fri 19-11-01																											
48		3.2		Future Conditions and Planned Improvements (1/2)	90 days	Mon 19-07-01	Fri 19-11-01																											
49			1	<a href="#">Existing and Future Conditions Memo (Draft)</a>	0 days	Fri 19-11-01	Fri 19-11-01																											
50		3.1		Existing Conditions Analysis (2/2)	70 days	Mon 20-01-13	Fri 20-04-17																											
51		3.2		Future Conditions and Planned Improvements (2/2)	70 days	Mon 20-01-13	Fri 20-04-17																											
52			2	<a href="#">Existing and Future Conditions Memo (Final)</a>	0 days	Fri 20-04-17	Fri 20-04-17																											
53		4		<b>Future Service Vision</b>	70 days	Mon 19-10-21	Fri 20-01-24																											
54		4.1		Strategic Corridor Identification	70 days	Mon 19-10-21	Fri 20-01-24																											
55		4.2		Strategic Service Planning and Network Integration	70 days	Mon 19-10-21	Fri 20-01-24																											
56			1	<a href="#">Future Monterey Bay Area Network Service Vision Memo (Draft)</a>	0 days	Fri 20-01-24	Fri 20-01-24																											
57		5		<b>Network Modeling</b>	205 days	Mon 19-10-21	Fri 20-07-31																											
58		5.1		Scenario Development	85 days	Mon 19-10-21	Fri 20-02-14																											
59		5.2		Analysis of Simulation Modelling Results	95 days	Mon 20-01-27	Fri 20-06-05																											
60			2	<a href="#">Future Monterey Bay Area Network Service Vision Memo (Final)</a>	1 day	Fri 20-07-31	Fri 20-07-31																											
61		6		<b>Governance Models</b>	165 days	Mon 20-02-10	Fri 20-09-25																											
62		6.1		Current Jurisdictional and Funding Arrangements	45 days	Mon 20-02-10	Fri 20-04-10																											
63			1	<a href="#">Governance and Operations Models Memo (Draft)</a>	0 days	Fri 20-04-10	Fri 20-04-10																											
64		6.2		Potential Future Governance Models	120 days	Mon 20-04-13	Fri 20-09-25																											
65		6.3		Potential Future Operator Models	120 days	Mon 20-04-13	Fri 20-09-25																											
66			2	<a href="#">Governance and Operations Models Memo (Final)</a>	0 days	Fri 20-09-25	Fri 20-09-25																											
67		7		<b>Implementation Planning</b>	265 days	Mon 20-03-09	Fri 21-03-12																											
68		7.1		Cost Estimate (1/2)	70 days	Mon 20-06-08	Fri 20-09-11																											
69			1	<a href="#">Cost Estimate Memo (Draft)</a>	0 days	Fri 20-09-11	Fri 20-09-11																											
70		7.1		Cost Estimate (2/2)	20 days	Mon 20-09-14	Fri 20-10-09																											
71			2	<a href="#">Cost Estimate Memo (Final)</a>	0 days	Fri 20-10-09	Fri 20-10-09																											
72		7.2		Ridership Analysis (1/2)	145 days	Mon 20-03-09	Fri 20-09-25																											
73			3	<a href="#">Ridership Results Memo (Draft)</a>	0 days	Fri 20-09-25	Fri 20-09-25																											
74		7.2		Ridership Analysis (2/2)	30 days	Mon 20-09-28	Fri 20-11-06																											



Project: 20200203_TAMC Proj Date: Thu 21-02-11	Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Manual Progress	
	Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline			
	Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Progress			

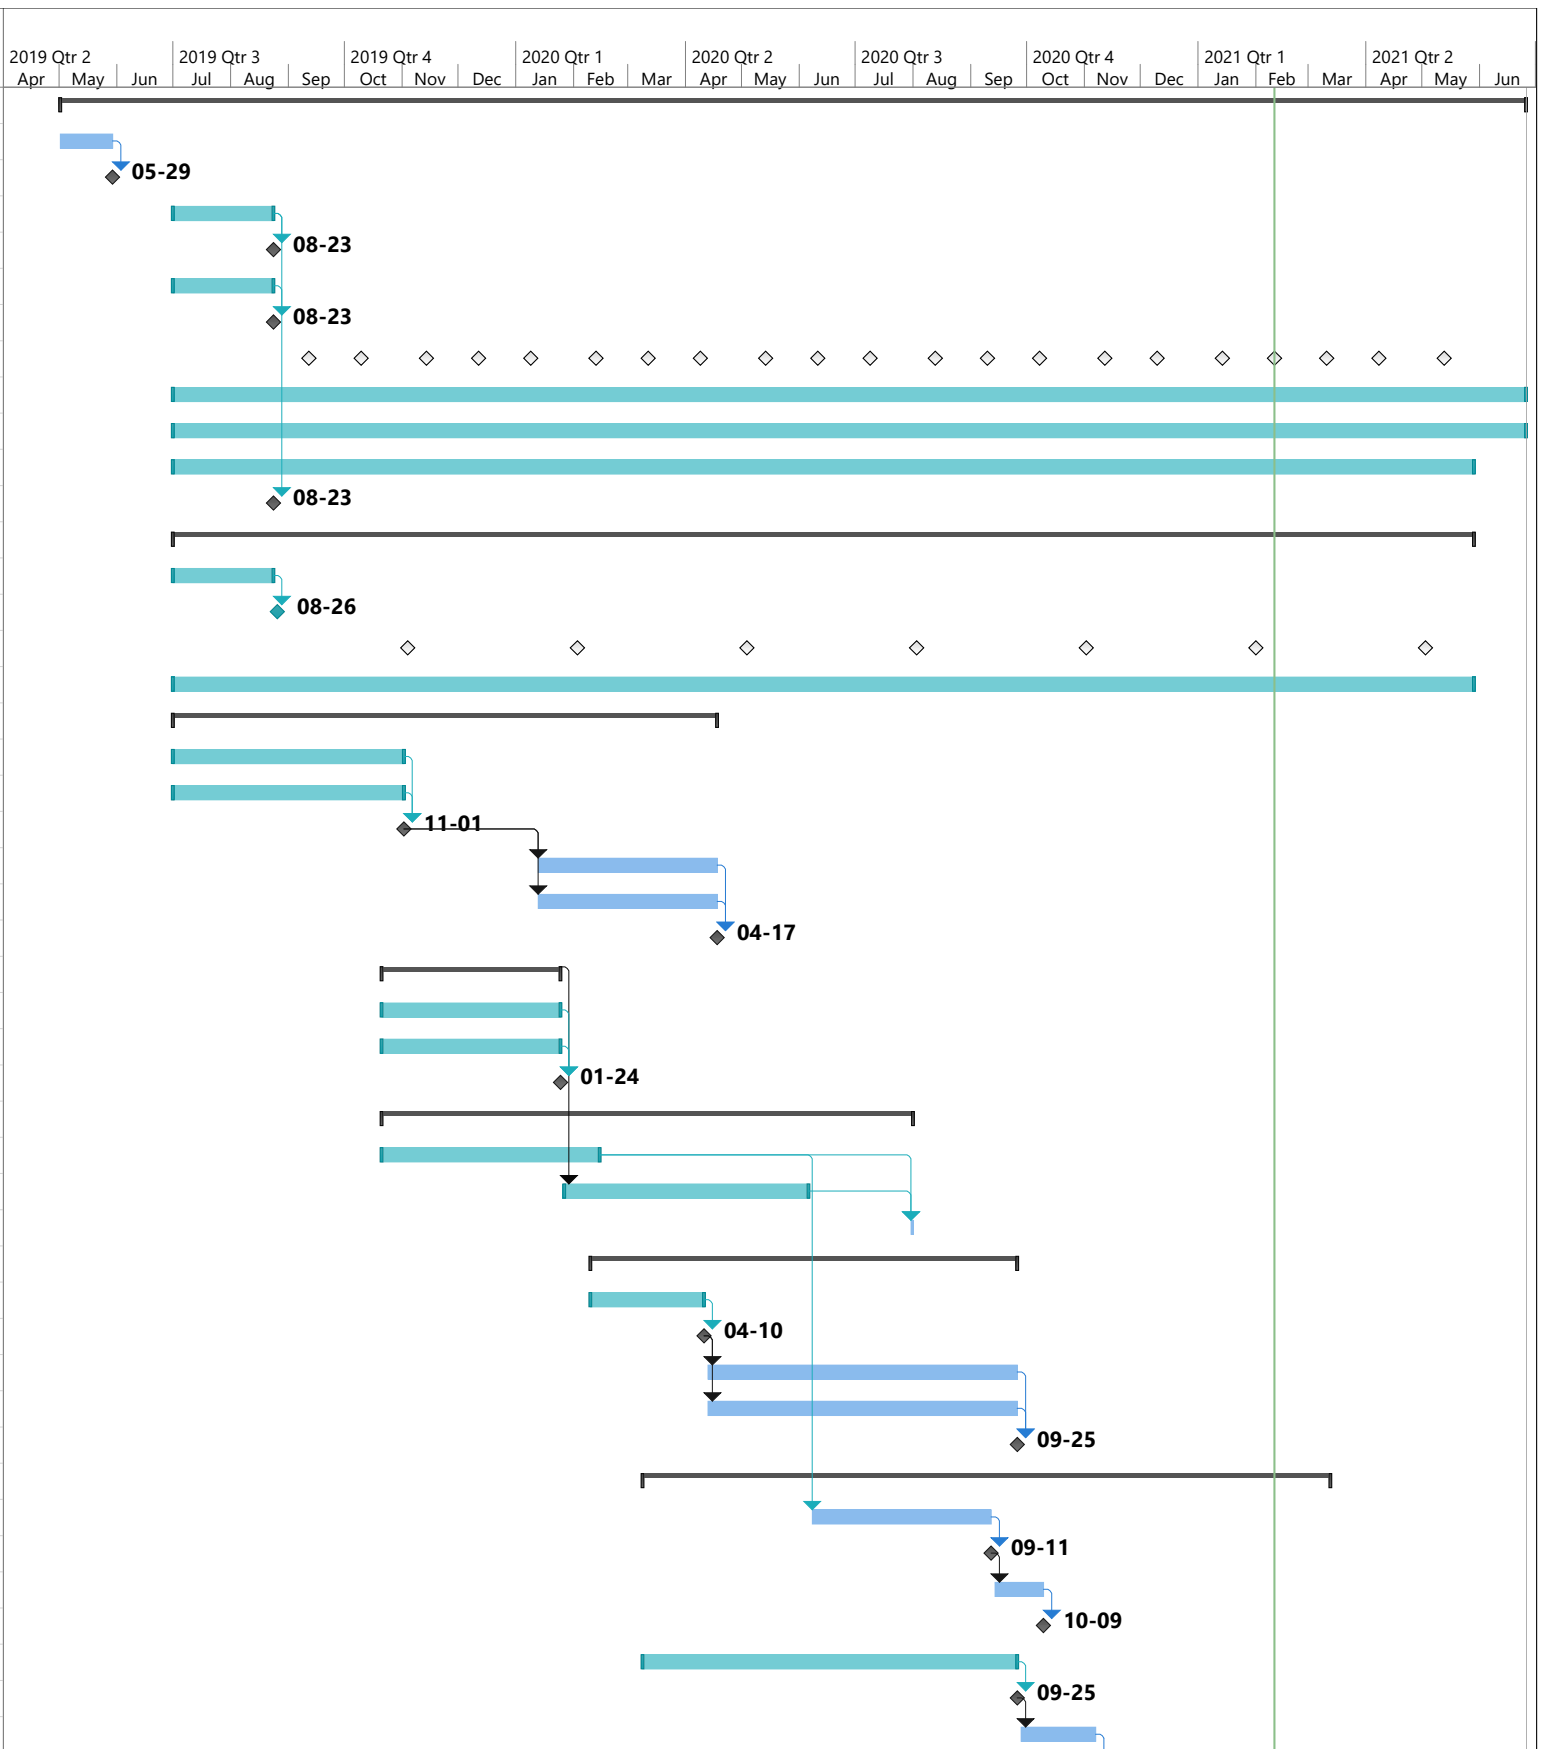
